

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	06 October 2026
Team ID	SWTID-2026-5440
Project Name	Auto Ticket Classification using Flow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Environment Setup	USN-1	As an admin, I can set up the ServiceNow instance with the roles and users needed for the school IT helpdesk.	2	High	Team Member 1
Sprint-1		USN-2	As an admin, I can define the incident categories (Network, Hardware, Account Access, Performance, General).	3	High	Team Member 2
Sprint-1		USN-3	As an admin, I can create a keyword table that maps keywords to categories.	5	High	Team Member 3
Sprint-1	Incident Submission	USN-4	As a student or teacher, I can submit an incident with a short description and a description.	3	High	Team Member 4
Sprint-1	Flow Trigger	USN-5	As an admin, I can create a Flow Designer flow that starts when a new incident is created.	5	High	Team Member 1
Sprint-1	Incident Submission	USN-6	As a user, I receive the incident number as confirmation after I submit a request.	2	Medium	Team Member 4
Sprint-2	Keyword Classification	USN-7	As the system, I can read the keywords in the incident's short description.	5	High	Team Member 3
Sprint-2		USN-8	As the system, I can also read the keywords in the description field.	3	High	Team Member 3
Sprint-2		USN-9	As the system, I can set the category to Network for Wi-Fi / internet keywords.	3	High	Team Member 2
Sprint-2		USN-10	As the system, I can set the category to Hardware for projector / display keywords.	3	High	Team Member 2
Sprint-2		USN-11	As the system, I can set the category to Account Access for password / login / locked keywords.	3	High	Team Member 4
Sprint-2		USN-12	As the system, I can set the category to Performance for slow / hang / freeze keywords.	3	Medium	Team Member 1
Sprint-3	Category Update & Routing	USN-13	As the system, I can set the category to General when no keyword matches.	2	High	Team Member 3
Sprint-3		USN-14	As the system, I can update the incident category automatically after classification.	3	High	Team Member 1
Sprint-3		USN-15	As the system, I can assign the incident to the right support group based on its category.	5	High	Team Member 2
Sprint-3		USN-16	As the system, I can set the incident priority from urgent keywords (e.g. exam, urgent).	3	Medium	Team Member 4
Sprint-3	Notifications	USN-17	As an IT staff member, I am notified when a ticket is assigned to my group.	2	Medium	Team Member 2
Sprint-3		USN-18	As a caller, I am notified of the category my ticket was given.	2	Medium	Team Member 4
Sprint-3	Incident View	USN-19	As an IT staff member, I can view the classified incidents in a filtered list.	3	Medium	Team Member 1
Sprint-4	Testing	USN-20	As a tester, I can run the flow on sample tickets for every category and check the results.	5	High	Team Member 3

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-4		USN-21	As a developer, I can fix wrongly classified tickets by refining the keywords.	3	High	Team Member 1
Sprint-4	Reporting	USN-22	As IT staff, I can see a dashboard of tickets per category.	5	Medium	Team Member 2
Sprint-4	Maintenance	USN-23	As an admin, I can add or edit keywords in the table without changing the flow.	2	Medium	Team Member 4
Sprint-4	Documentation & Release	USN-24	As a team, we prepare a user guide and a demo of the solution.	3	Low	Team Member 3
Sprint-4		USN-25	As a team, we move the finished flow to the final ServiceNow instance.	2	Medium	Team Member 1

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	20	6 Days	12 Oct 2026	17 Oct 2026		
Sprint-2	20	6 Days	19 Oct 2026	24 Oct 2026		
Sprint-3	20	6 Days	26 Oct 2026	31 Oct 2026		
Sprint-4	20	6 Days	02 Nov 2026	07 Nov 2026		
Total	80	24 Days				

Velocity:


Each sprint is 6 days long and the team's velocity is 20 story points per sprint. The team's average velocity (AV) per iteration unit (story points per day) is:

$$AV = \text{velocity} / \text{sprint duration} = 20 / 6 = \mathbf{3.33 \text{ story points per day}}$$

Total project: 80 story points over 4 sprints (24 days), so the planned burn rate is about 3.33 points per day.

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time. The chart below shows the planned (ideal) burndown for the four sprints; actual progress can be added as each sprint finishes.

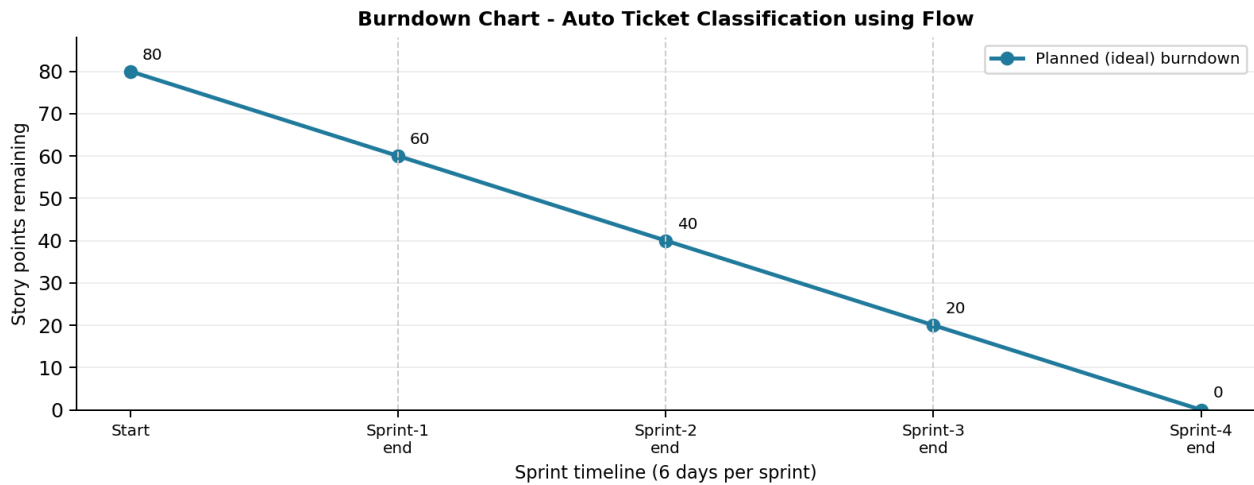

<https://www.visual-paradigm.com/scrum/scrum-burndown-chart/>

<https://www.atlassian.com/agile/tutorials/burndown-charts>

Reference:

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>

<https://www.atlassian.com/agile/tutorials/epics>

<https://www.atlassian.com/agile/tutorials/sprints>

<https://www.atlassian.com/agile/project-management/estimation>

<https://www.atlassian.com/agile/tutorials/burndown-charts>
